ID	Task Name	Duration	Start	Finish	3 WK
135	Cut 30" pipe @ vac relief valve and repair mortar	1 day	Wed 8/31/16	Wed 8/31/16	Yes
136	Weld 4" pipe @ Vac relief valve & Collar	1 day	Thu 9/1/16	Thu 9/1/16	Yes
137	Repair coating	1 day	Fri 9/2/16	Fri 9/2/16	Yes
138	Form & Set rebar - 30" Pipe support	1 day	Fri 9/2/16	Fri 9/2/16	Yes
139	Pour pipe support & Encasement @ VRV	1 day	Tue 9/6/16	Tue 9/6/16	Yes
140	Backfill & Install valve	1 day	Wed 9/7/16	Wed 9/7/16	Yes
219	Set N E/W Header	16 days	Fri 8/12/16	Fri 9/2/16	Yes
220	Set S E/W Header	16 days	Fri 8/12/16	Fri 9/2/16	Yes
223	Install Aqua Ammonia 3-way Valve	2 days	Wed 8/24/16	Thu 8/25/16	Yes
224	Remove/Replace Lighting	108 days	Thu 4/21/16	Thu 9/22/16	Yes
226	1/2" CLS - DE Storage Room	2 days	Wed 8/31/16	Thu 9/1/16	Yes
234	Procure piping modifications materials (Estimated)	13 days	Wed 8/17/16	Fri 9/2/16	Yes
236	Demolish existing pump and pad	2.5 days	Tue 9/6/16	Thu 9/8/16	Yes
237	Install Anchor Bolts	1 day	Thu 9/8/16	Fri 9/9/16	Yes
238	Set New pump	1 day	Fri 9/9/16	Mon 9/12/16	Yes
239	Modify Pipe connections	2 days	Mon 9/12/16	Wed 9/14/16	Yes
240	Grout pump	1 day	Wed 9/14/16	Thu 9/15/16	Yes
241	Cure Grout	5 days	Thu 9/15/16	Thu 9/22/16	Yes
242	Lead electric conduit/testing filter 1	5 days	Wed 9/14/16	Wed 9/21/16	Yes
243	Lead electric conduit/testing filter 2	5 days	Wed 9/21/16	Wed 9/28/16	Yes
245	Demolish existing pump and pad	2 days	Wed 9/28/16	Fri 9/30/16	Yes
246	Install Anchor Bolts	1 day	Fri 9/30/16	Mon 10/3/16	Yes
247	Set New pump	1 day	Mon 10/3/16	Tue 10/4/16	Yes
248	Modify Pipe connections	2 days	Tue 10/4/16	Thu 10/6/16	Yes
249	Grout pump	1 day	Thu 10/6/16	Fri 10/7/16	Yes
250	Cure Grout	5 days	Fri 10/7/16	Fri 10/14/16	Yes
251	Lead electric conduit/testing filter 10	5 days	Thu 10/6/16	Thu 10/13/16	Yes
252	Lead electric conduit/testing filter 9	5 days	Thu 10/13/16	Thu 10/20/16	Yes
303	Erect scaffold	2 days	Mon 9/26/16	Tue 9/27/16	Yes
304	FW Gallery Wall - Fab	2 days	Wed 9/28/16	Thu 9/29/16	Yes
306	Sawcut Door openings	1 day	Fri 9/30/16	Fri 9/30/16	Yes
307	Demo Exterior Door opening & Hypalons in FW Resorvoir	1 day	Mon 10/3/16	Mon 10/3/16	Yes

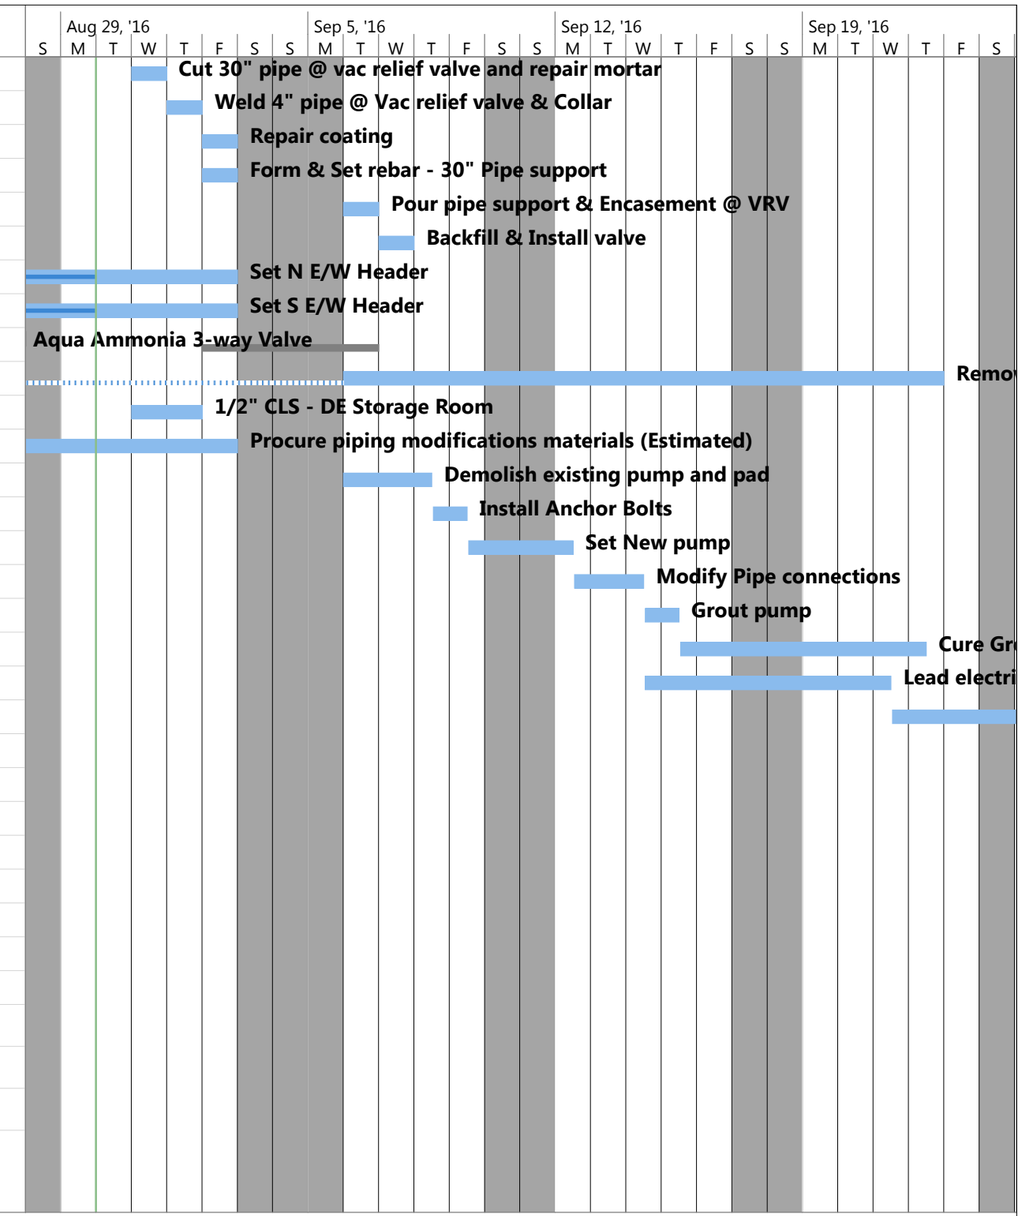

Project: Westlake Filtration Plan
Date: Tue 8/30/16

Task	Inactive Task	Manual Summary Rollup	External Milestone	Baseline Milestone
Split	Inactive Milestone	Manual Summary	Deadline	Baseline Summary
Milestone	Inactive Summary	Start-only	Critical	Progress
Summary	Manual Task	Finish-only	Critical Split	Manual Progress
Project Summary	Duration-only	External Tasks	Baseline	
